Activity ID	Activity Name	Original Duration	Start	Finish
LSC 23-015 Bid Sched Lymes' Senior Center - 1.9.2024		338	14-Sep-23 A	30-Dec-24
LSC 23-015 Bid Sched.PRE-CON Preconstruction Phase		205	14-Sep-23 A	26-Jun-24
LSC 23-015 Bid Sched.PRE-CON.DOCUMENT PREP Plan Review and Prep		95	14-Sep-23 A	24-Jan-24
LSC 23-015 Bid Sched.PRE-CON.BID Bidding and GMP Phase		37	09-Jan-24	28-Feb-24
LSC 23-015 Bid Sched.PRE-CON.PREP Prepatory Phase		85	29-Feb-24	26-Jun-24
LSC 23-015 Bid Sched.CONSTRUCTION Construction Phas		206	29-Feb-24	12-Dec-24
LSC 23-015 Bid Sched.CONSTRUCTION.Bldg Construction Building Const		201	29-Feb-24	05-Dec-24
CON170	Mobilize Project	0		29-Feb-24
CON175	Secure Site and Install Erosion Protection	5	29-Feb-24	06-Mar-24
CON190	Select Site Demolition for New Addition	3	07-Mar-24	11-Mar-24
CON180	Select Interior Demolition	10	12-Mar-24	25-Mar-24
CON185	Cut/Cap/Drop/Makesafe MEPs	10	12-Mar-24	25-Mar-24
CON200	Addition Excavate Foundations, Place, Damproof and Backfill	15	20-Mar-24	09-Apr-24
CON230	Select Demolition for Roof System	8	20-Mar-24	29-Mar-24
CON220	UG Plumb/Elec	5	10-Apr-24	16-Apr-24
CON240	BF/Prep for slabs	3	17-Apr-24	19-Apr-24
CON250	Radiant Piping in slab	5	22-Apr-24	26-Apr-24
CON260	Prep/Pour slabs on grade	5	29-Apr-24	03-May-24
CON300	Deliver Roof Truss Package	3	02-May-24	06-May-24
CON210	Framing and Structural Supports	20	06-May-24	31-May-24
CON310	Exterior Sheathing, Install Exterior Windows	10	23-May-24	05-Jun-24
CON330	Install Trusses, Roof Sheath and Dampproof	15	03-Jun-24	21-Jun-24
CON520	Install HVAC Equipment	10	19-Jun-24	02-Jul-24
CON590	New Roofing System	18	24-Jun-24	17-Jul-24
CON350	MEP Rough In	20	03-Jul-24	30-Jul-24
CON580	Exterior Doors, Windows, Siding and Trim	15	08-Jul-24	26-Jul-24
CON600	Gutter and Downspouts	5	29-Jul-24	02-Aug-24
CON360	Insulate and Sheetrock Walls and Ceilings	15	31-Jul-24	20-Aug-24
CON470	Install Light Fixtures	10	21-Aug-24	03-Sep-24
CON480	Tape and Finish Gypsum Wall Board	10	21-Aug-24	03-Sep-24
CON490	Prime & 1st Coat Paint	5	04-Sep-24	10-Sep-24
CON270	Interior Storefront installation	8	04-Sep-24	13-Sep-24
CON280	Operable partition install	10	11-Sep-24	24-Sep-24
CON500	Install ACT Gird System	5	16-Sep-24	20-Sep-24
CON510	Install In Grid MEP	15	23-Sep-24	11-Oct-24
CON570	Energize HVAC Systems and Lighting	10	14-Oct-24	25-Oct-24
CLO670	Trim and Energize Fire Alarm System	10	14-Oct-24	25-Oct-24
CON540	Install Millwork and Interior Trim	15	28-Oct-24	15-Nov-24
CON620	Install ceiling pads	8	28-Oct-24	06-Nov-24
CON560	Install Flooring	15	07-Nov-24	27-Nov-24
CON530	Finish Paint	10	18-Nov-24	29-Nov-24
CON550	Install Doors and Hardware	8	26-Nov-24	05-Dec-24
CON610	Install and Trim out Plumbing Fixtures	5	28-Nov-24	04-Dec-24

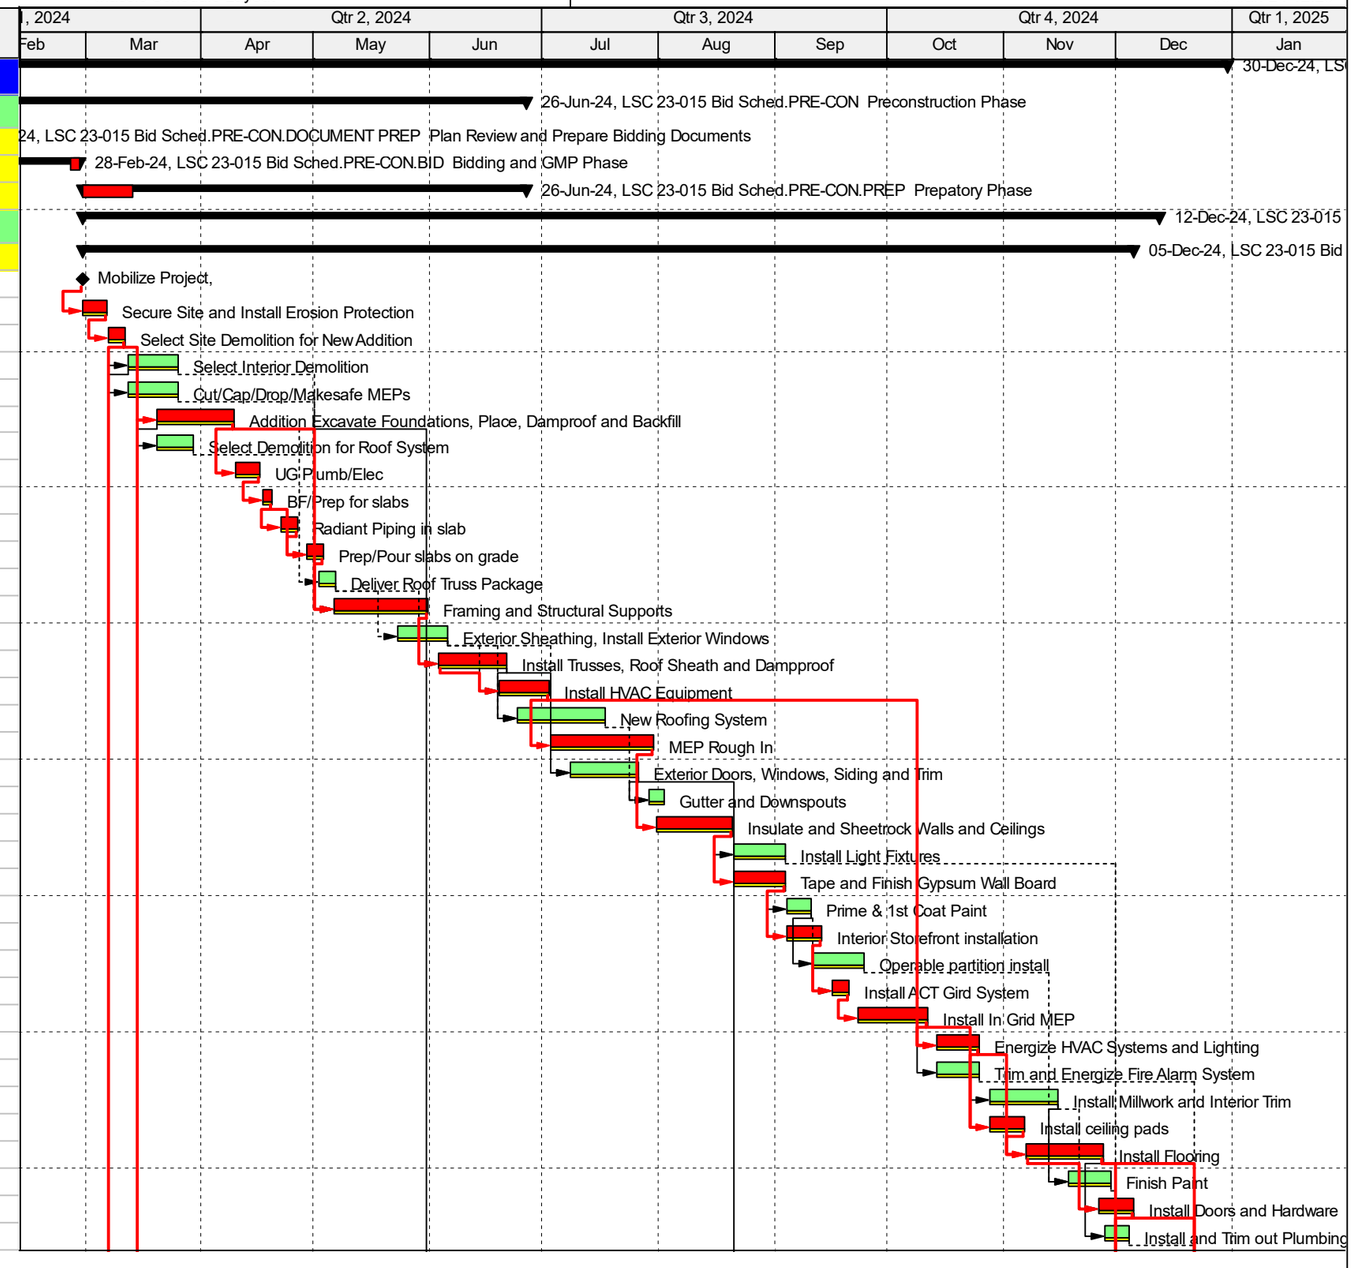

- Actual Level of Effort
- Primary Baseline
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- summary

Lymes' Senior Center Renovation

Newfield CONSTRUCTION
EXPERIENCE. WE BUILD ON IT.™

Activity ID	Activity Name	Original Duration	Start	Finish
LSC 23-015 Bid Sched.CONSTRUCTION.Site Improvement Sitework and Si		198	12-Mar-24	12-Dec-24
SITE1000	Selective Site Demo	5	12-Mar-24	18-Mar-24
SITE1010	Relocate Existing Sheds	3	15-Mar-24	19-Mar-24
SITE1020	Sanitary System Installation	10	05-Jun-24	18-Jun-24
SITE1030	Install Storm Drainage Systems	10	19-Jun-24	02-Jul-24
SITE1040	Install Fire Tank and Related Piping	12	03-Jul-24	18-Jul-24
SITE1050	Install Light Pole Bases and Conduit System	10	19-Jul-24	01-Aug-24
SITE1120	Install Fire Pump and Associated Piping, Wire System	20	19-Jul-24	15-Aug-24
SITE1080	Install Light Poles and Fixtures	7	02-Aug-24	12-Aug-24
SITE1130	Site Lighting Wiring	6	13-Aug-24	20-Aug-24
SITE1060	Grade and Boxout New Parking and Drives	15	26-Aug-24	13-Sep-24
SITE1070	Paving and Line Striping	8	16-Sep-24	25-Sep-24
SITE1100	Landscaping	10	26-Sep-24	09-Oct-24
SITE1090	Spread Topsoil and Seed	5	10-Oct-24	16-Oct-24
SITE1110	Remove Temporary Fencing and Restore	5	06-Dec-24	12-Dec-24
LSC 23-015 Bid Sched.Closeout Closeout Phase		17	06-Dec-24	30-Dec-24
CLO650	Initiate Punchlist and Implement	15	06-Dec-24	26-Dec-24
CLO635	Final Cleaning	5	06-Dec-24	12-Dec-24
CLO640	Final Inspections	2	27-Dec-24	30-Dec-24
CLO660	Substantial Completion	0		30-Dec-24

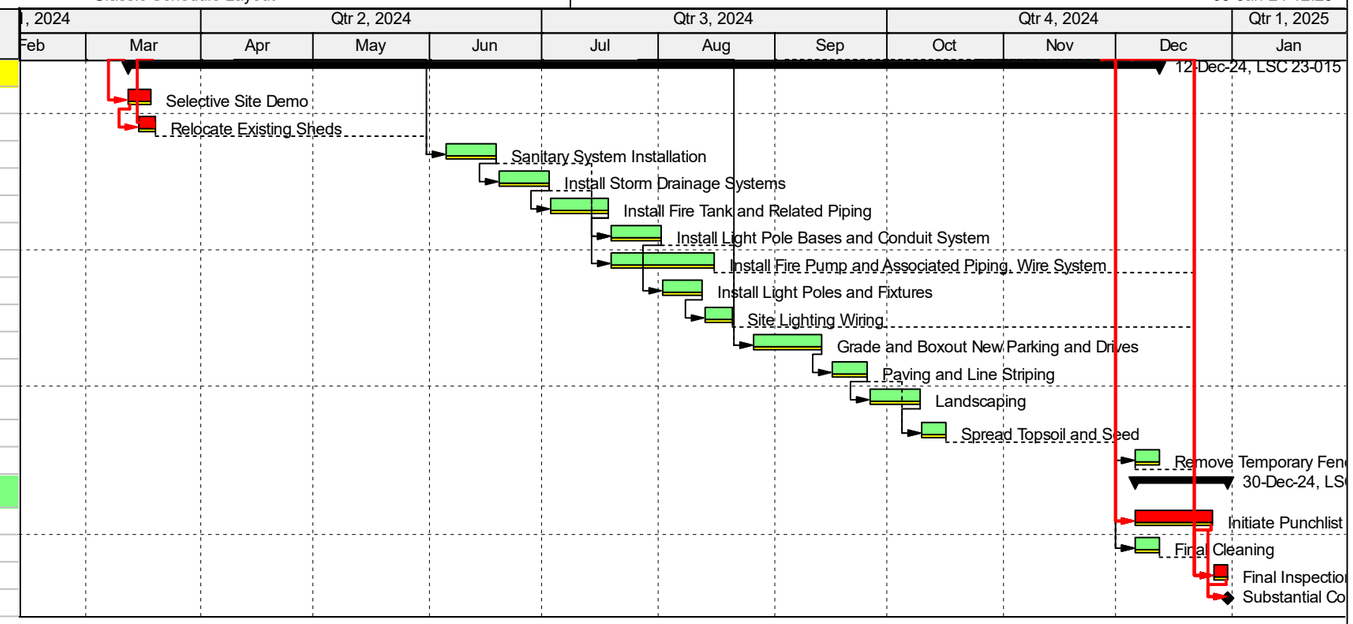

Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Lymes' Senior Center Renovation

Newfield CONSTRUCTION
EXPERIENCE. WE BUILD ON IT.™
